




### St George's Way eastern approach to Bermuda Bridge

Contractor is continuing the works along St George's Way to prepare the route in readiness to open the Bermuda Bridge to motorised vehicles. The works involve installation of new tactile pavers laid, reseating of manhole lids and renewing kerbs and footways.

### Eastern embankment approach to Bermuda Bridge

The southern footway on Bermuda Bridge has been completed and was opened for the use of pedestrians and cyclists. Works on laying new tarmacadam surfacing in the carriageway will be completed upon completion of the works in St George's Way.

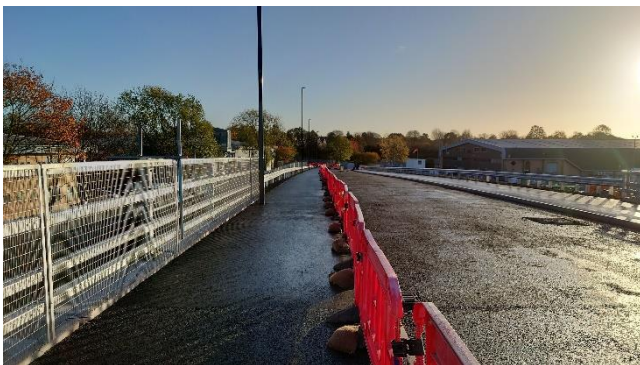

### Bermuda Bridge Works

Structural works on the bridge are completed new waterproofing and tarmacadam binder courses have been laid on the carriageway. Carriageway final surface course and road markings will be installed prior to opening the bridge to motorised vehicles.

### Western embankment approach to Bermuda Bridge

Earthworks along the southeast section of the western approach embankment are completed and new safety barrier is completed in readiness to construct the final surface to the roadway. A new filter drain is currently being installed at the foot of the embankment to manage rainwater run-off whilst new vegetation becomes established.





### Barling Way and The Bridleway

Backfilling works in Barling Way will be completed following completion of works on STW apparatus to new footway levels to enable the footway in Barling Way to be completed. Whilst backfilling of The Bridleway has been completed and the carriageway constructed awaiting final surface course.



**Relocation of Gas Governor by Phoenix Centre**  
Works by CADENT to relocate an existing gas governor in the island close to the Phoenix Centre to a nearby location outside of the proposed new road alignment have continued. These works are planned to be completed by end of November 2023, which will then enable the construction of new bus stop and road layout by Phoenix Centre.



**Works at bend in Bermuda Road by Hazel Way**

CADENT will commence works on the shallow gas main following completion of the works by Phoenix centre. The new road layout will then be constructed.

