



**St George’s Way eastern approach to Bermuda Bridge**

Subject to further inspection the contractor has completed the minor remedial works in St George’s Way and has also commenced remedial works on the gabion wall by Bermuda Parkway Station which is planned to be finished by end of February 2024. The new road surfacing and road markings have been added.



**Eastern embankment approach to Bermuda Bridge**

The footways on Bermuda Bridge were completed and opened for the use of pedestrians and cyclists since end of October 2023. The contractor has also completed the final surface course and road markings on the eastern approach to the bridge no further works are anticipated to the roadway.



**Bermuda Bridge Works**

The contractor has completed the final surface course and road markings on the eastern approach to the bridge no further works are anticipated to the bridge.

### Western embankment approach to Bermuda Bridge

The contractor has also completed the final surface course and road markings on the western approach to the bridge up to its junction with The Bridleway.




### Barling Way and The Bridleway

STW have completed works on their existing apparatus and Barling Way has been constructed to binder level in readiness of surface course. The water leak at the top of Barling Way footway has been repaired and therefore it can be surfaced. The roadway will be finished following completion of works on Bermuda Road by The Phoenix Centre.



### Road works along Bermuda Road

Works on the construction of new bus stop and road layout by Phoenix Centre commenced the first week of December 2023.

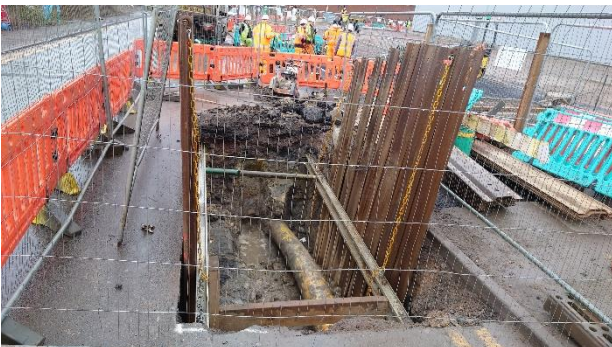

### CADENT works along Bermuda Road

CADENT have installed a new gas governor by Phoenix Centre and backfilled the excavation and continued with a new gas main along Bermuda Road to connect the gas governor to the existing gas main by Hazel Way. These works are planned to be completed in early February 2024.

